COLLINS CONTRACTORS LTD

METHOD STATEMENT

Ref No.:

Description of the Task/Activity:	Temporary support works				
Project Name:	53 Warminster Road SE25 4DQ		**Project Ref:**		
Site Address/ Location:	53 Warminster Road SE25 4DQ		**Start Date/Time:**	10 2022	
			Finish Date/Time:		
Personnel involved:	**Name**		**Role/Trade**		
	Paul Haughey		Site Manager		
	Jake Jinks		Metalworker		
Works Supervisor:	Adam Rich	**Role:**	Contract Manager	**Tel:**	07973 323552
Key Plant and Tools Required:	Standard hand tools				
Key Materials Required:	Standard construction items for the general works as in the schedule				
Other Essential Equipment:	Nonspecific for the general works				
Specific Identified Residual Hazards: (or refer to the task specific risk assessment(s))	Refer to initial works RAMS Uncontrolled collapse				
Specific Staff Training Requirements:	Sub-contractors will have trade specific competency training				


Sequence of Operations: (Specifying methods of working, tools, materials and equipment utilised)	Those carrying out works activities shall have had a suitable site induction. Operatives will have a briefing on this method statement and associated risk and COSHH assessments. Operatives will have signed to the task specific RA attached Refer to the drawing job no. 27266 sheet S-00220 dated 28 06 2022 by Cluttons for detail of materials and layout. Further and additional details are as at S-00225 dated 11 10 2022 as to fixing detail The materials will be hoisted up to the scaffold level adjacent to the works area and shall be stored in the building. At flat B Remove ceiling to enable installation of anchor beam to purlins as at S-00223. Support with acrows during installation. The two internal posts and the external horizontal channel shall be pre drilled or drilled on site to accommodate the tie rods The two internal posts shall be manually lifted into position and affixed top and bottom to the joists with bolts as indicated on drawing 0224 Note the requirement for a steel plate as at drawing A-00220 attached to the wall with chemical anchors Timber packing will be installed as required Note steel strap as shown at base of transfer post and tie rod through at top again attached as per drawing S-00224 to run to anchor beam as at S-00223 as above Base noggins to be installed for post support The external channel may be positioned as shown at S-00220 and held in place with temporary timber supports/packers cut to size The threaded bar is to be fed through and wing nuts tightened to secure beams. Retain temporary support timbers Note the restraint channel may not be removed until the purlins are propped and all loading is removed from the top of the chimney breast At flat A the rear existing purlin is to be strapped to the valley timber see S-00223
Temporary Supports and Props needed to facilitate the works:	As detailed above

COLLINS CONTRACTORS LTD

Method of Access and Egress to the work area:	Via scaffold ladders and current indoor premises ways					
Fall Protection Measures: (Where work at height cannot be eliminated - consider both Personnel & Materials)	Edge protection					
Hazardous Substances: (Attach COSHH Assessments and MSDS)	(ie: Lubricants/Solvents/Flammable Materials/Refrigerants/Welding Gases etc)					
	 **Toxic**	 **Harmful/ Irritant**	 **Corrosive**	 **Dangerous for the environment**	 **Oxidising**	
Applicable:	**No**	**No**	**No**	**No**	**No**	
Hazardous Substances continued	 **Long term health hazard**	 **Flammable**	 **Compressed gas**	 Explosive		
Applicable	**No**	**No**	**No**	**No**	**Yes/No**	
SWL's:	(Detail any limits on the loadings applicable to temporary plant/equipment or fixed elements of the structure where the work is taking place.) NA					
Required Personnel Protective Equip.: General but see specific task RAs and COSHH RAs	 Safety Boots	 Hard Hats	 Safety Gloves	 Hearing Protection	 Respiratory Protection	 Eye Protection	**Other:** 1. Hi-Viz 2. 3.
	Yes	**Yes**	**Yes**	**No**	**Yes**	**Yes**	
Emergency Procedures:	Alert supervisor					

First Aid Facilities:	**Name of On-Site First Aider:**	Paul Haughey
	First Aid Box Location:	At the welfare
	Location of Nearest Hospital:	Croydon University Hospital 530 London Road CR7 7YE

COLLINS CONTRACTORS LTD

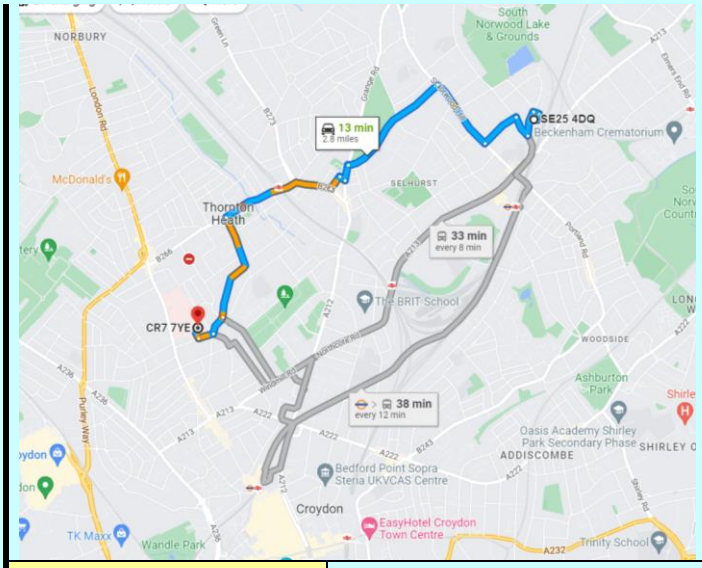

Other Information & Comments:	Substances to be used are to be identified and COSHH assessments provided

All work will be undertaken by qualified competent persons with experience of the type of work described above, and in all cases in full accordance with safety procedures specified in the company's Health and Safety Policy.

Prepared by: **R Pressley**

Position: H & S Manager **Date: 18 10 2022**

Reviewed by: **Adam Rich**

Position: Contracts Manager **Date: 18.10.2022**

Briefing delivered by:

Position:

Date:

We (the undersigned) have read and understood the attached method statement and will comply with the specified requirements and control measures. If the work activity

changes or deviates from that originally envisaged, we will seek further advice and request an amended method statement.

Name (Print)	Signature	Date
